


CONSTRUCTION UPDATE

On November 1, 2013, the Rt. Hon. Herb Gray Parkway team announced that approximately 300 girders placed on-site at the Parkway will be removed and replaced with new girders and that a revised construction schedule would be developed.

- The project team understands the impact this large construction project has had on the community and the Windsor Essex Mobility Group and Parkway Infrastructure Constructors have **re-sequenced the schedule in a way that allows them to work quickly and efficiently toward overall project completion.**
- The key to the schedule, subject to final approval, is the **focus on prioritizing the connection of neighbourhood streets across the Parkway.**
- The **re-sequenced schedule is based on seasons.** As the opening dates for cross-roads approach, more detailed information will become available.
- Details on the schedule are available on www.hgparkway.ca and continued updates will be easily readable on the construction interactive map available on the website homepage.


Re-sequenced Construction Schedule

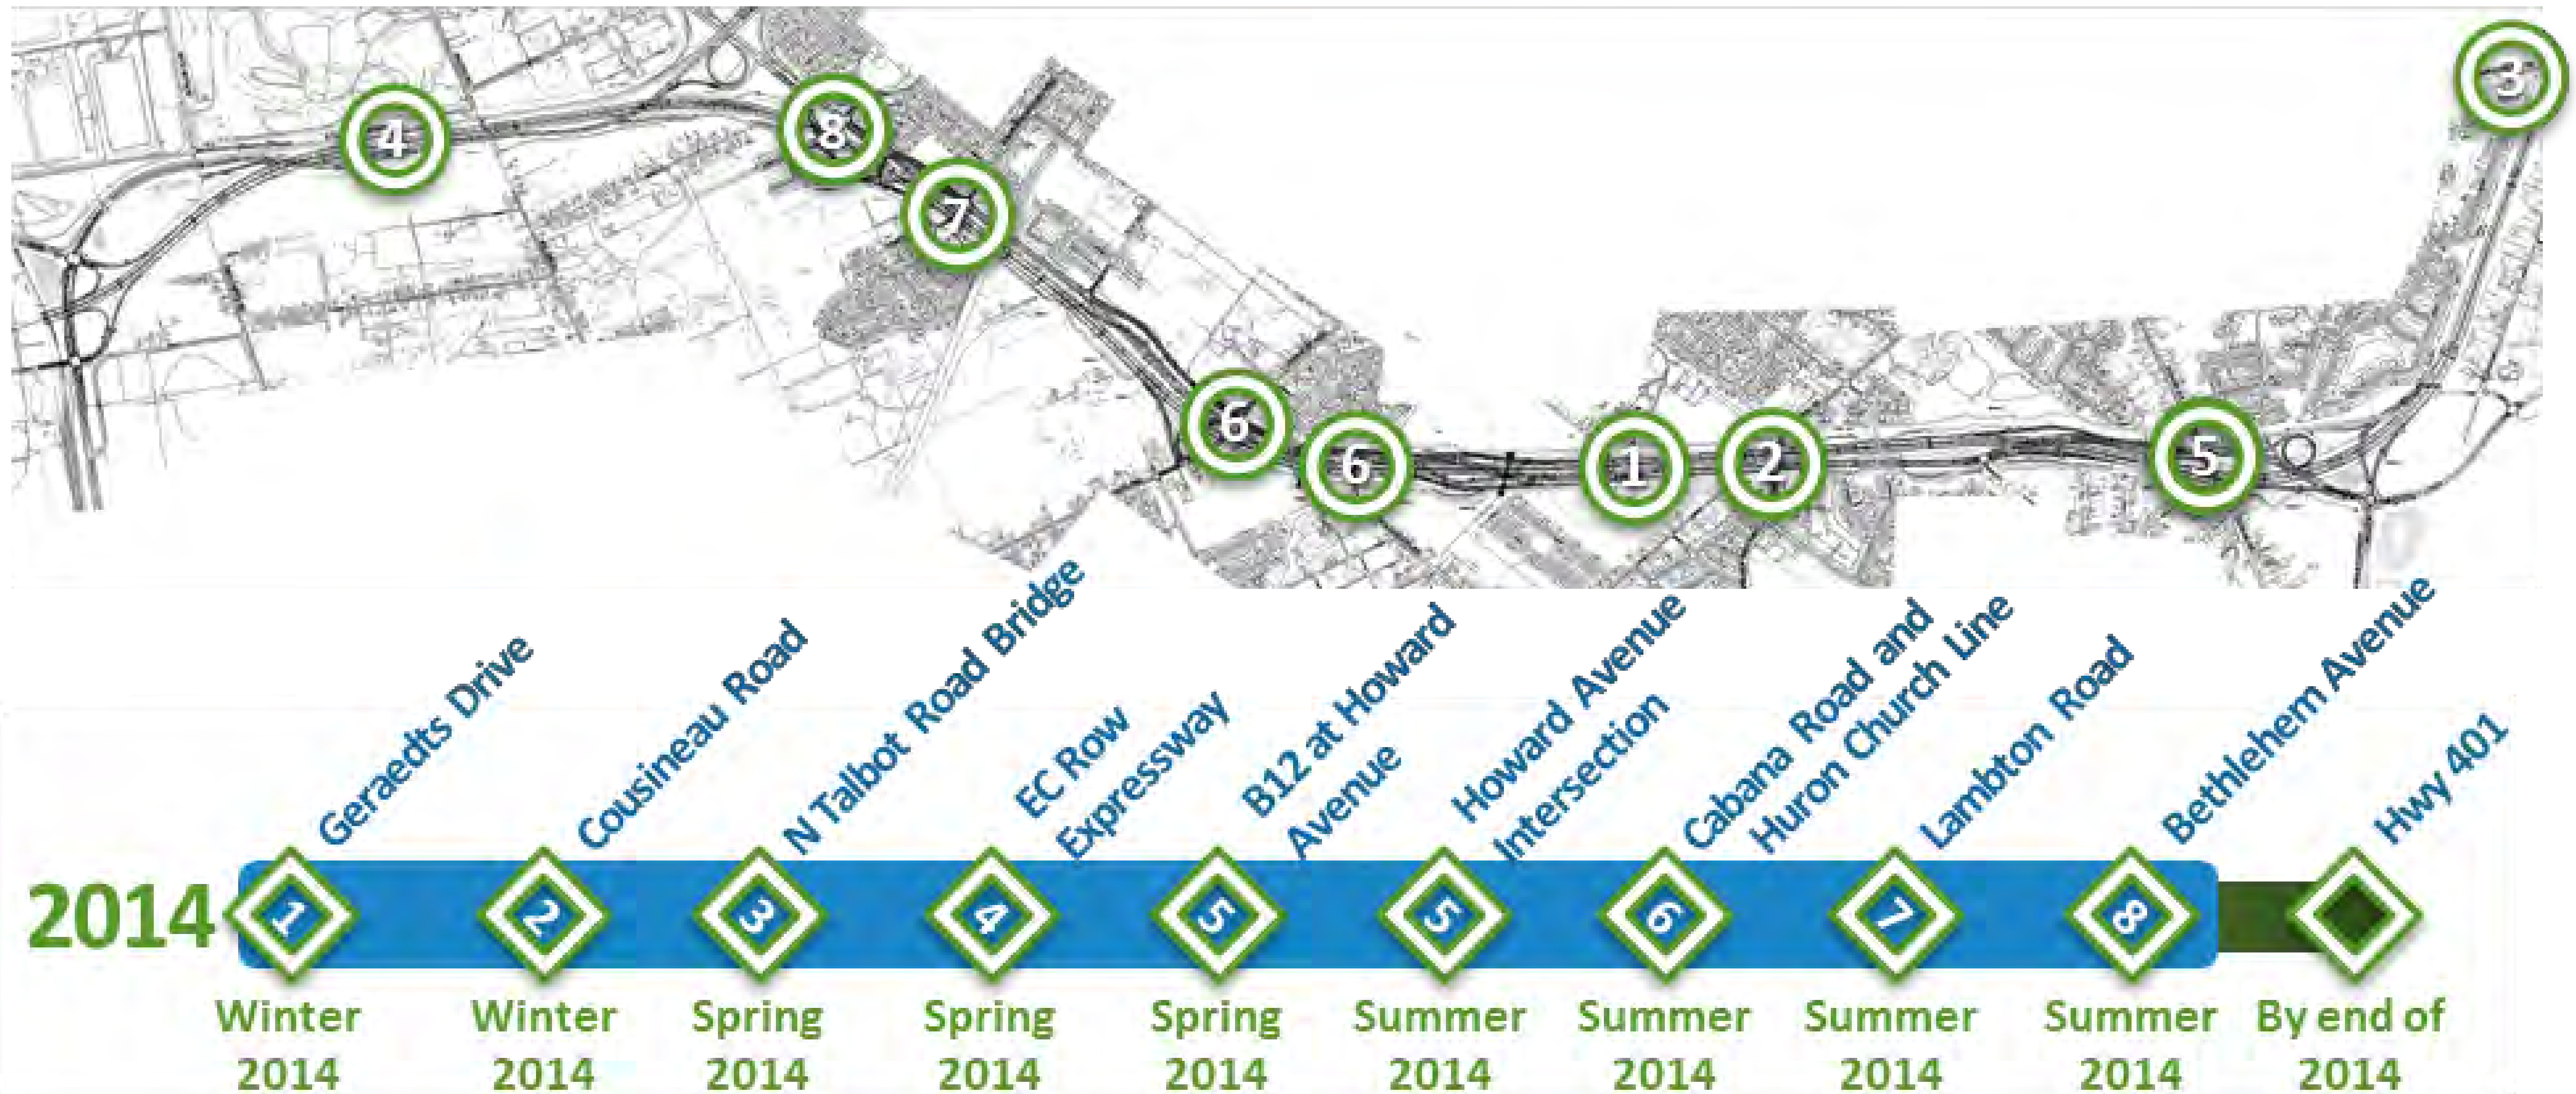



Girder removal will occur over the **next 3 months** at Tunnels 2 (LaBelle Tunnel), 5 (Oakwood Tunnel) and 7 (Villa Borghese Tunnel) and Bridge 15 (North Talbot Road Bridge).

- Neighbouring residents will receive notices before the removal work begins.
- For Tunnels 5 and 7, removal will involve cranes lifting the girders and placing them on flatbed trucks for hauling.
- At Tunnel 2 and at the North Talbot Road Bridge, removal will include removal of the concrete decks and parapets and then cranes will lift the girders and place them on flatbed trucks for hauling.
- Efforts will be made to limit noise, dust and impacts on traffic.
- All work will proceed in accordance with municipal noise by-laws.


When	October 25, 2013 for approximately 6 months
Why	For the construction of Bridge-12
How	<ul style="list-style-type: none"> Access from Highway 3 to Howard Avenue will be through the roundabout to County 9 (Howard Diversion), to Howard Connector

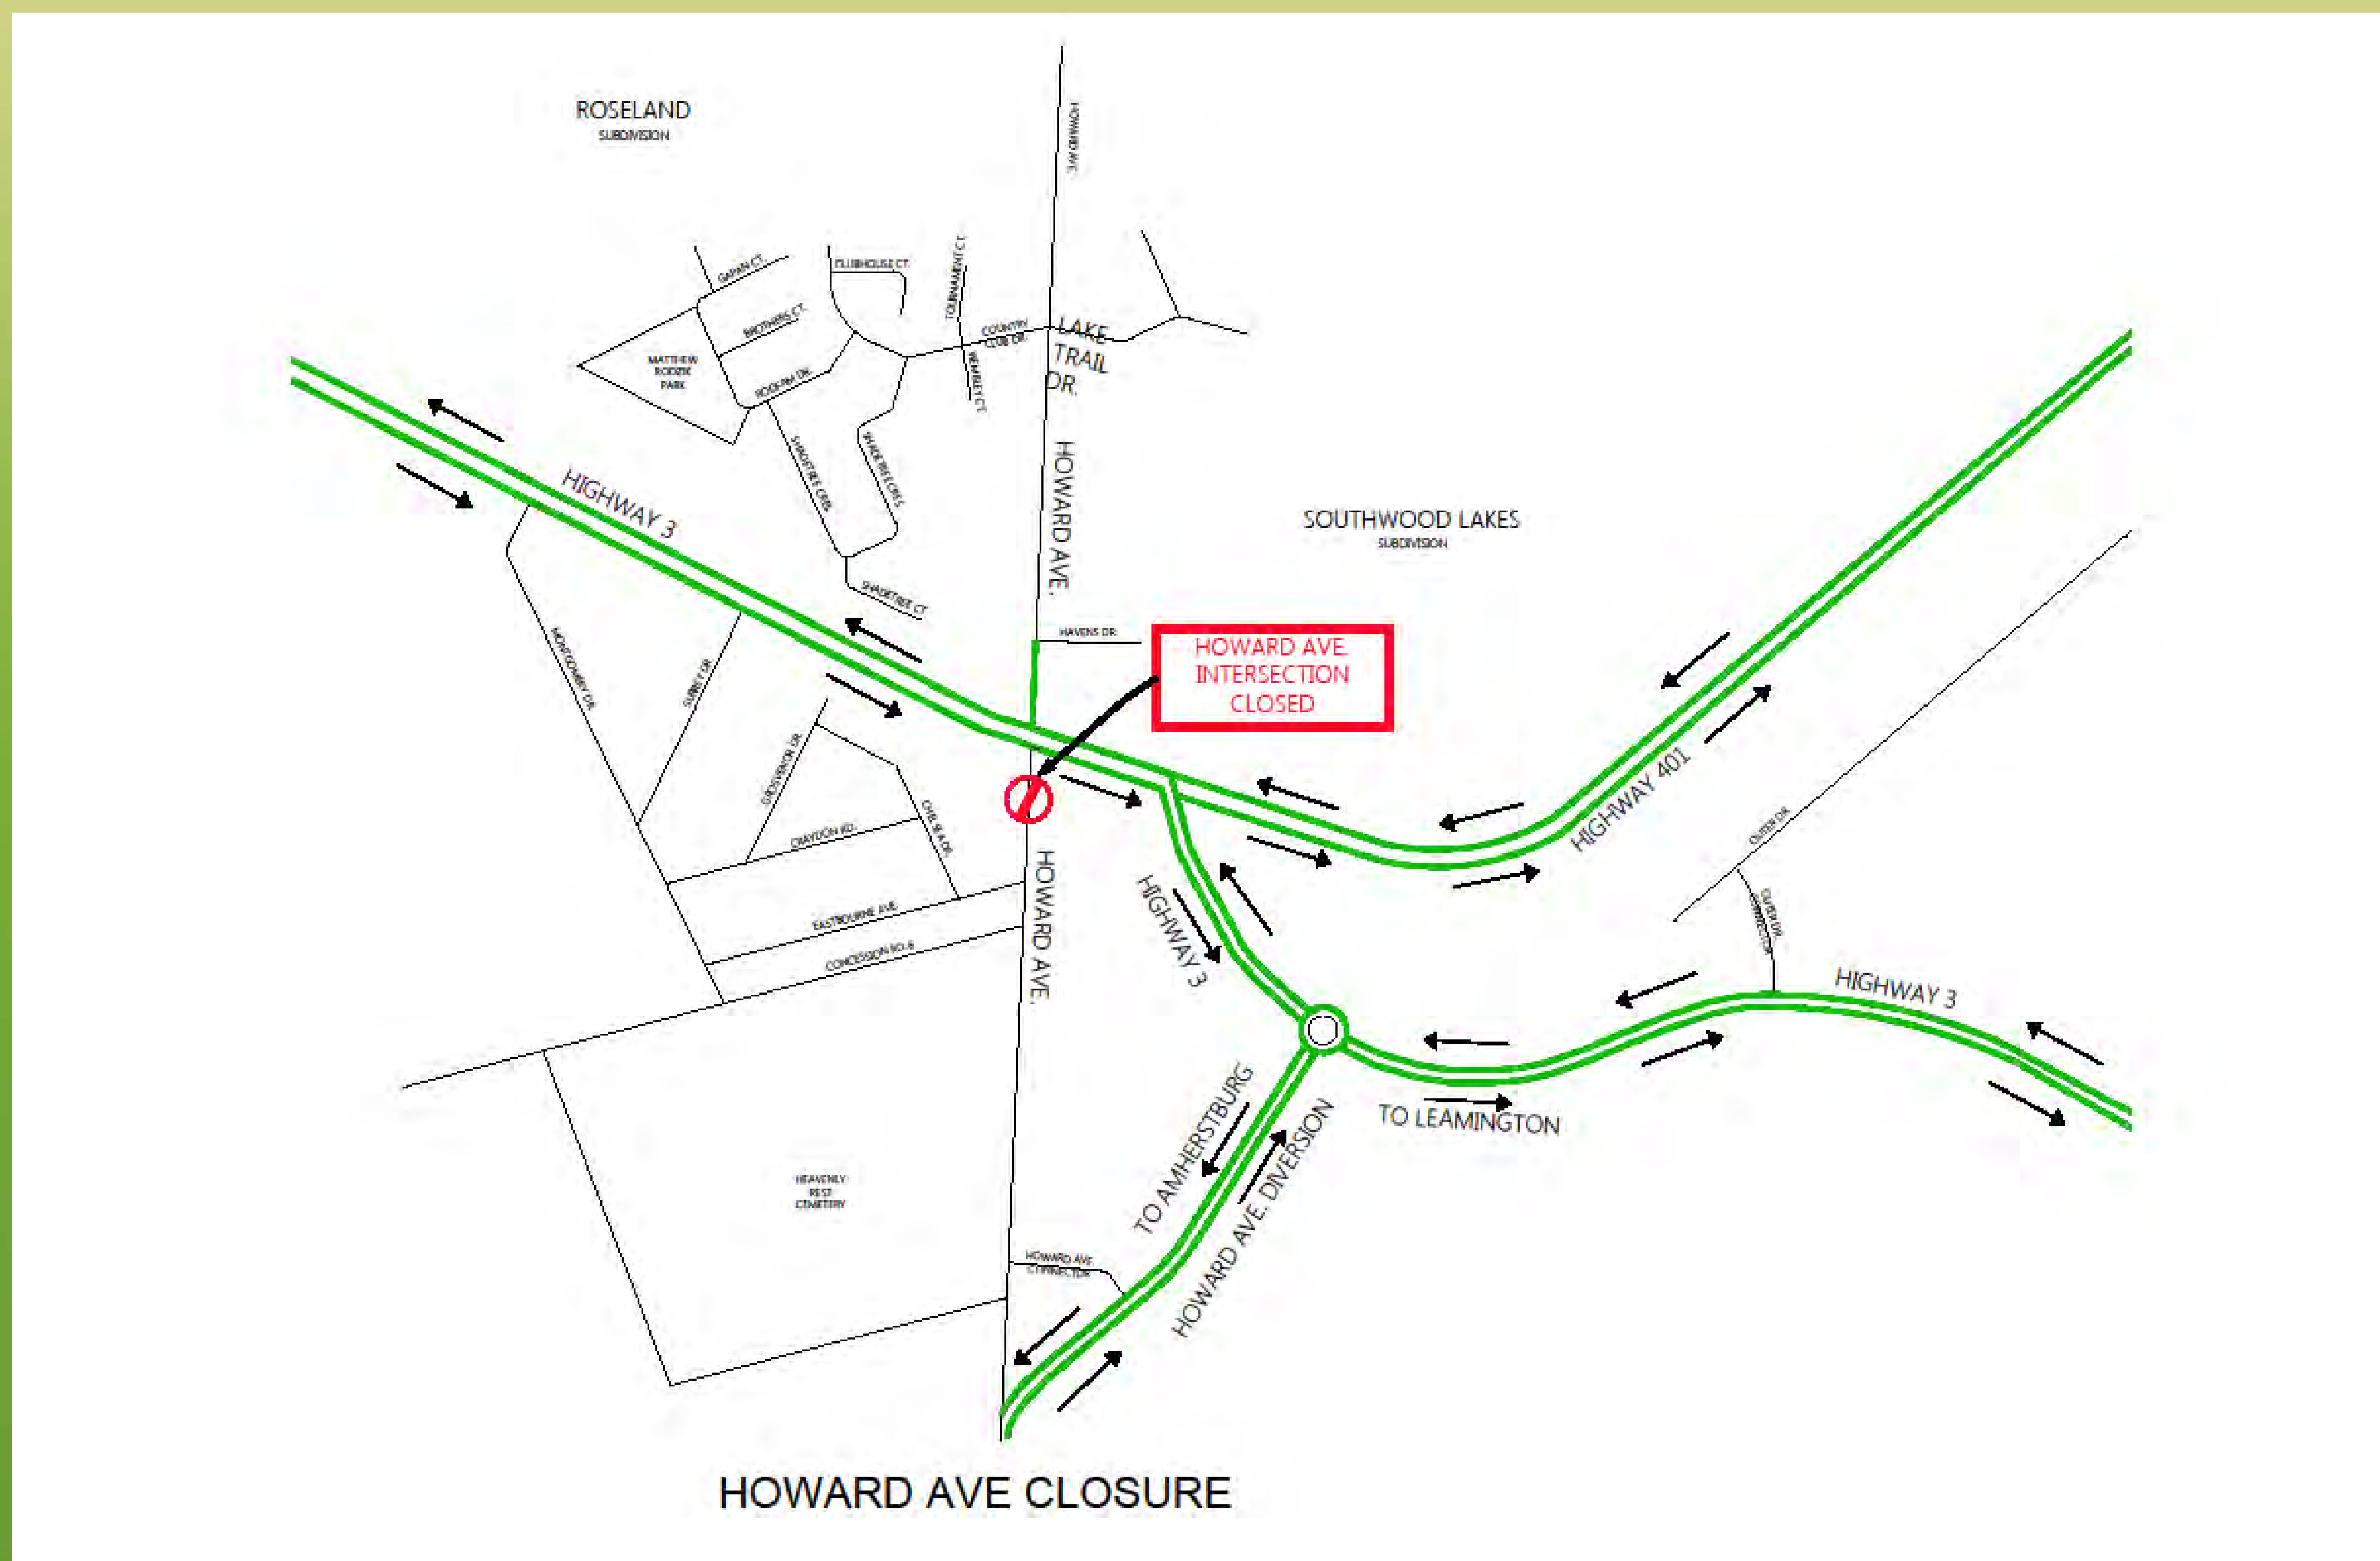

When	Starting late 2013 - early 2014 for approximately 6 months
Why	Re-construction of Ojibway Parkway
How	<ul style="list-style-type: none"> Ojibway Parkway will not be closed but single laned Traffic will flow on the westbound lanes while re-constructing the eastbound lanes. Once the eastbound lanes are re-constructed, traffic will be shifted to them to allow the re-construction of the westbound lanes There might be specific short closures of the intersections during this period

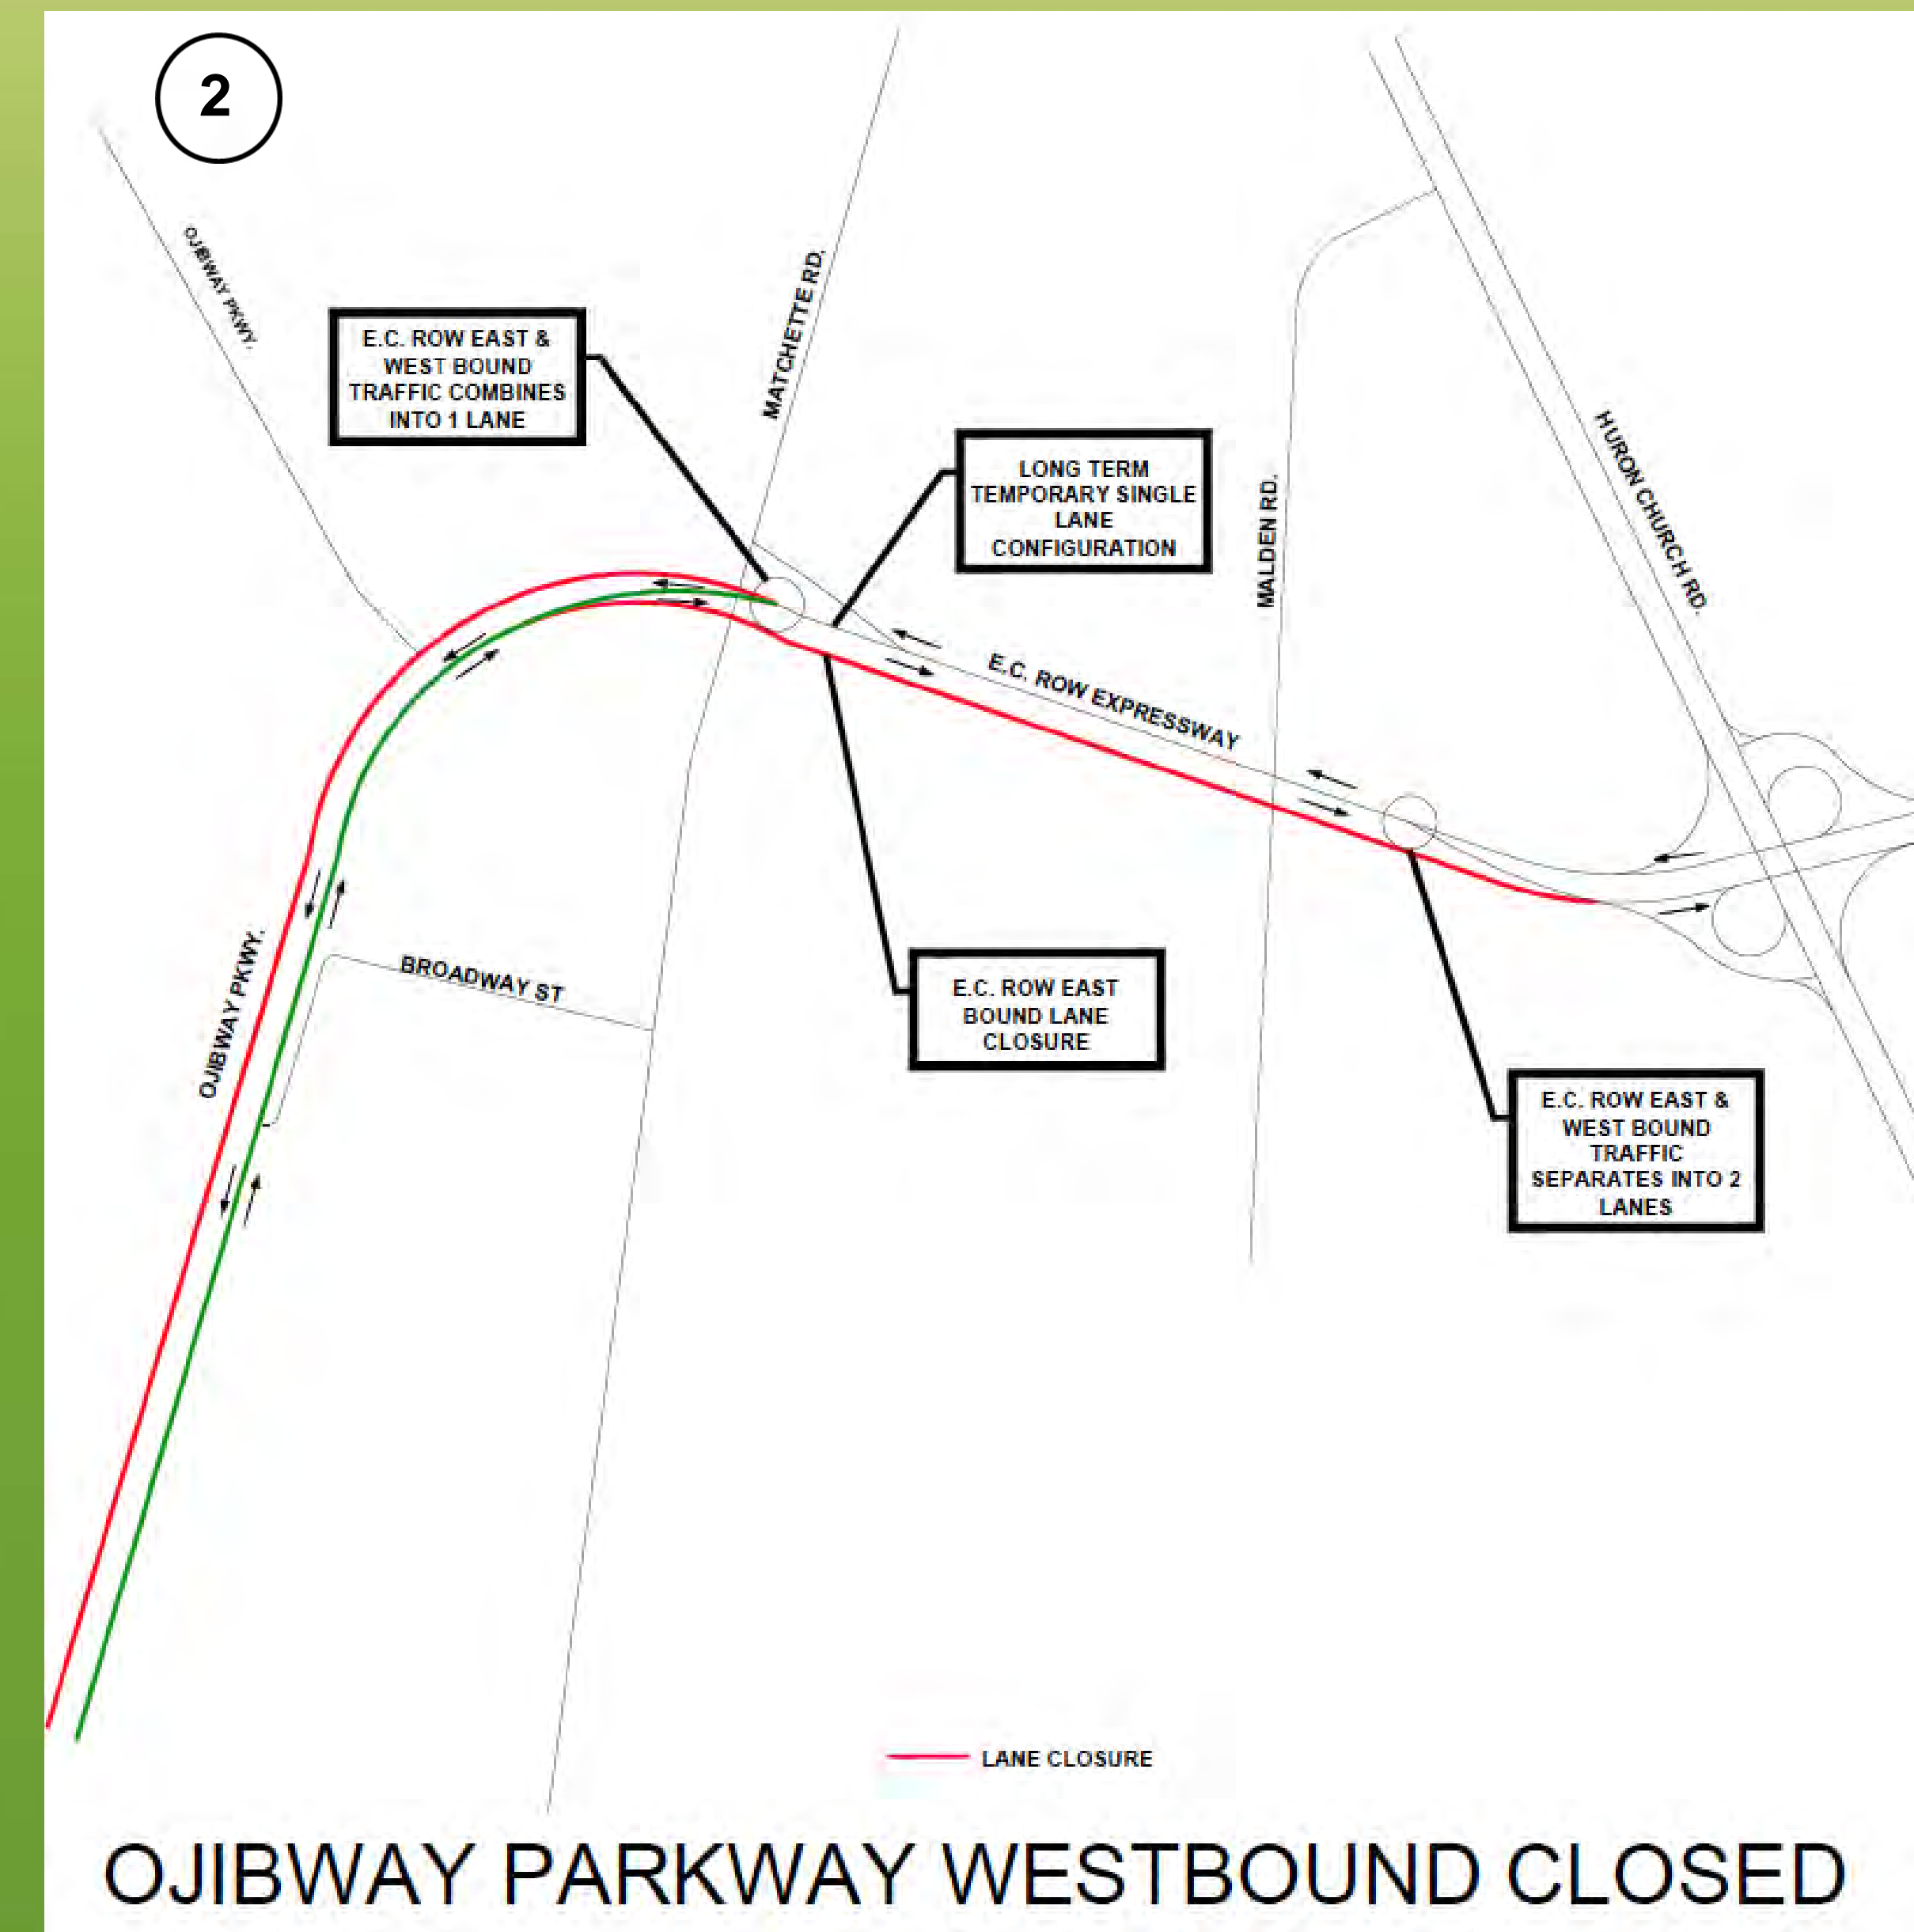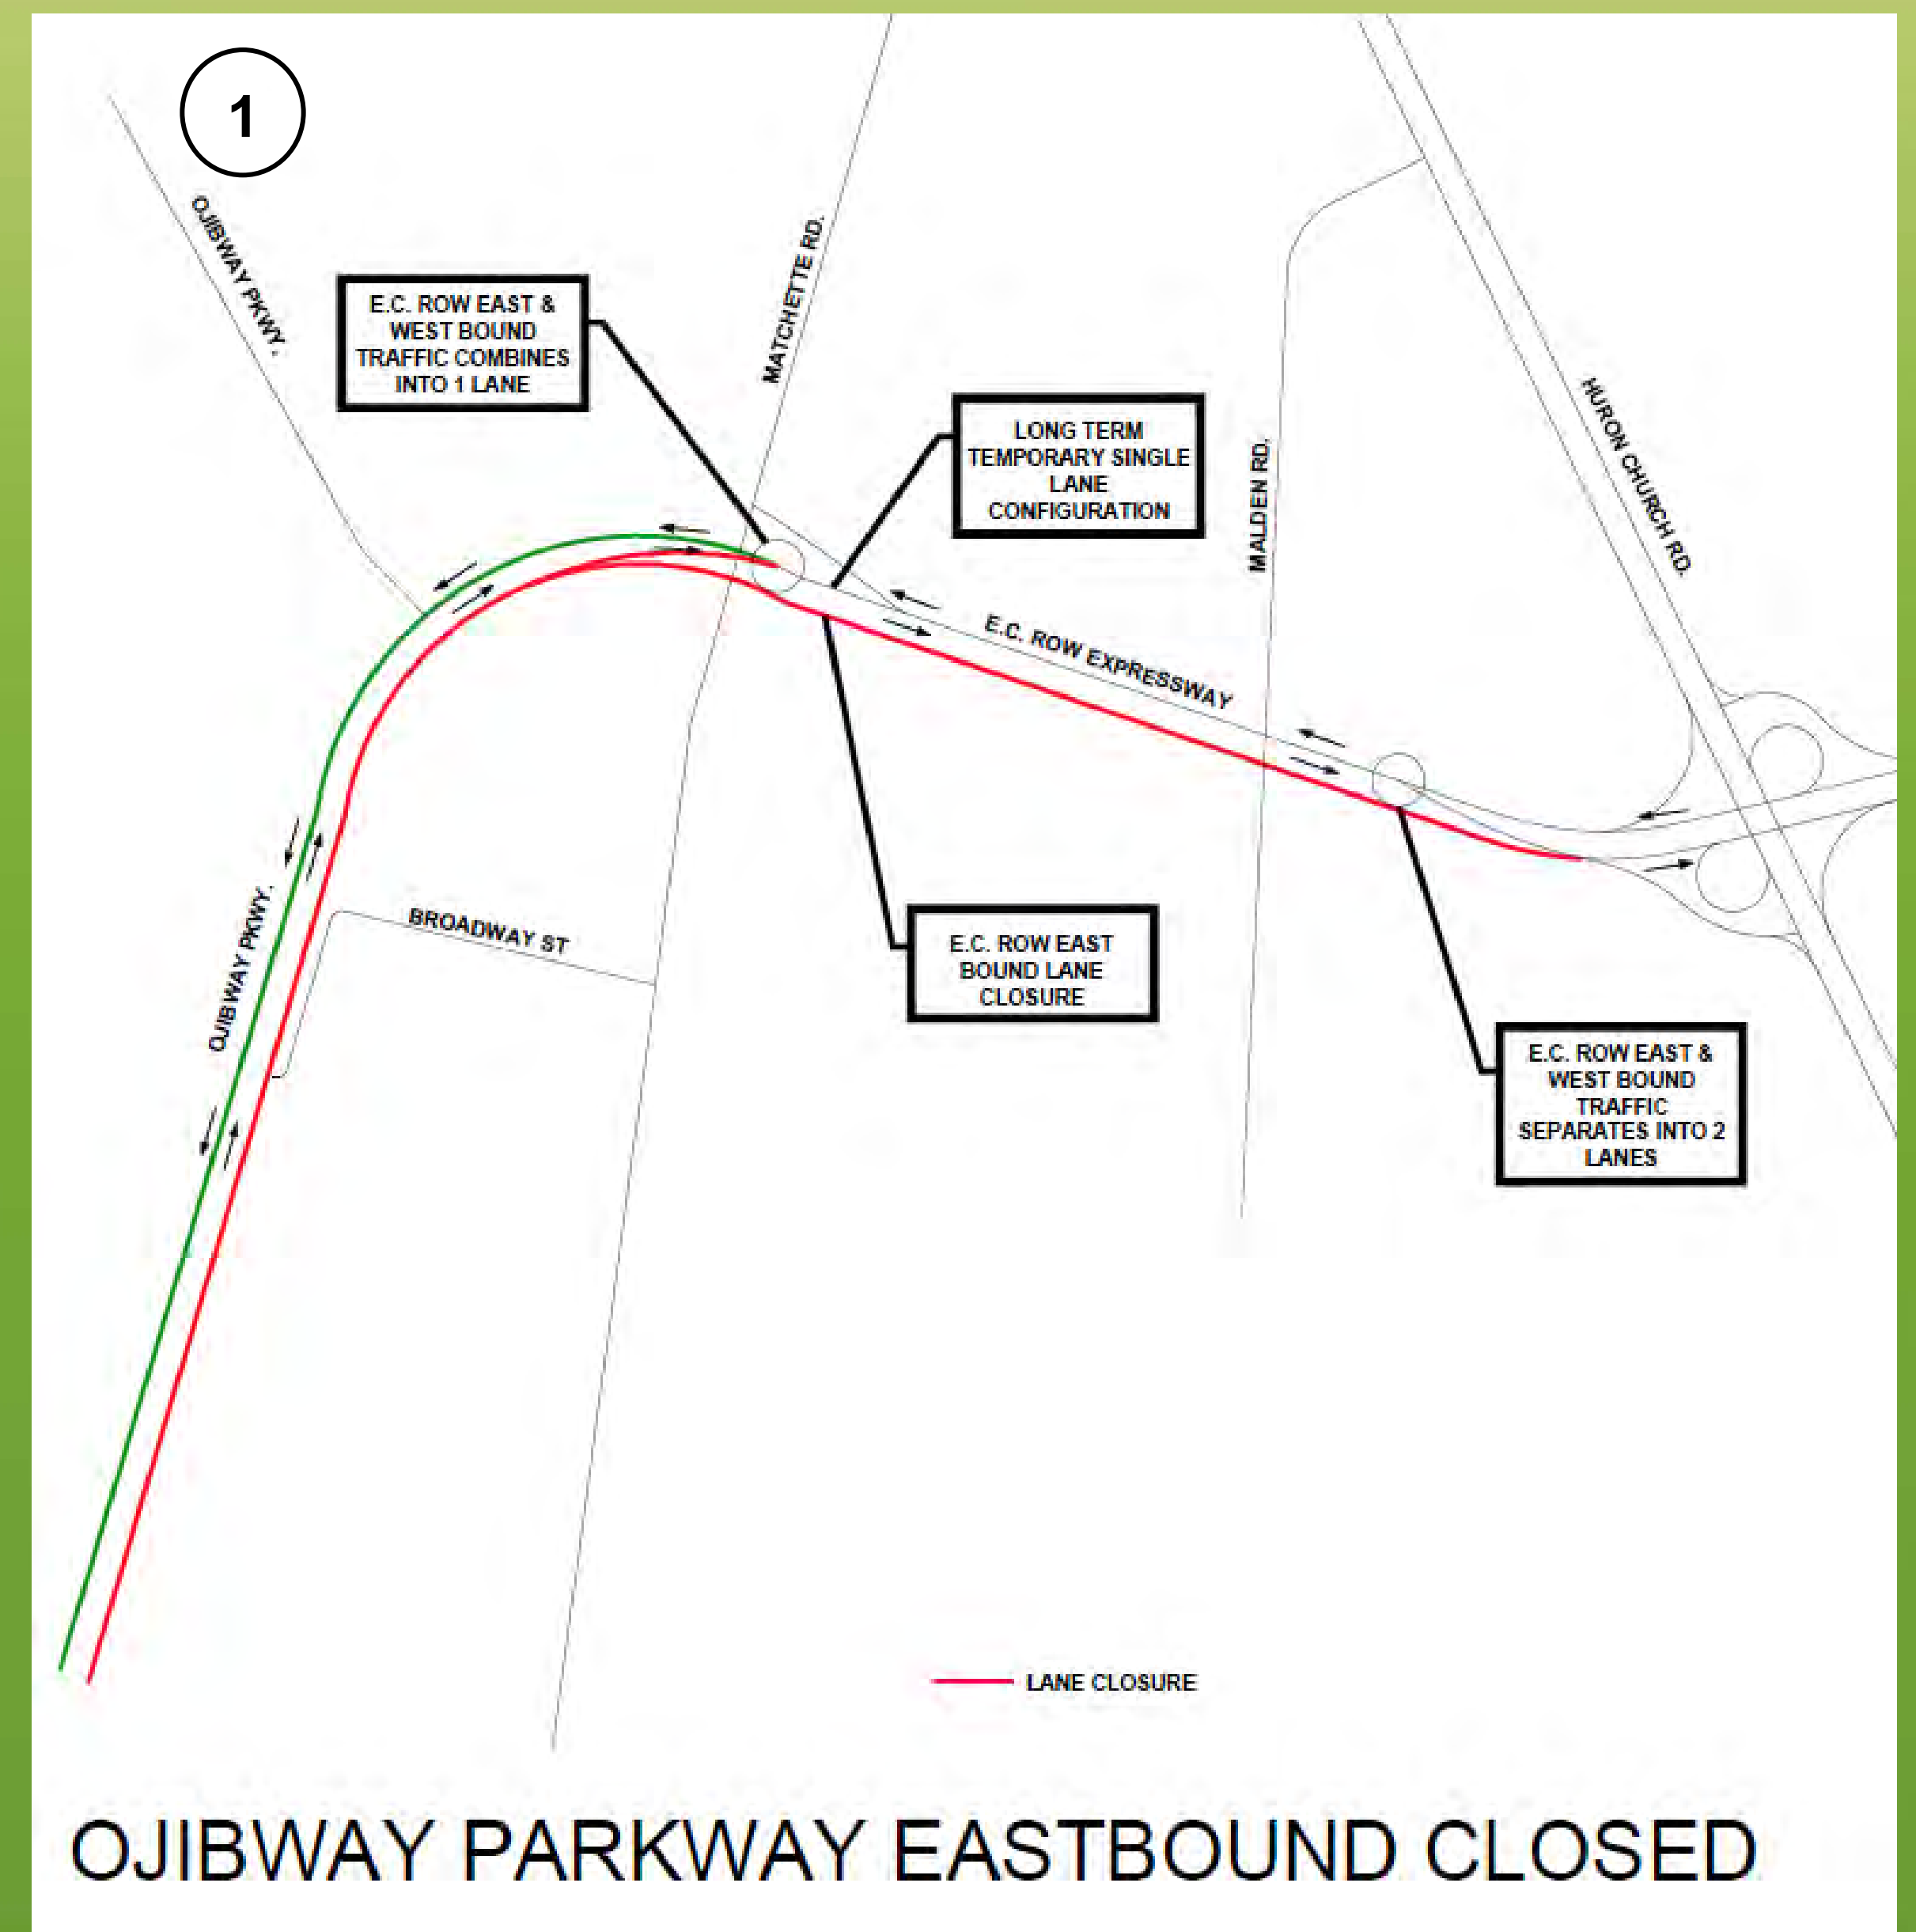

When	March 2014 (estimated)
Why	For the re-construction of the off-ramp at Huron Church
How	<p>The proposed detour routes for trucks, subject to further review and consultation, during this period may be:</p> <ul style="list-style-type: none"> - Southbound trucks: E. C. Row Expressway to Walker Road, Walker Road to Provincial Road, Provincial Road to Highway 401 - Northbound trucks: E. C. Row Expressway to Dougall Avenue, Dougall Avenue/Ouellette Street to Tecumseh Road, Tecumseh Road to Huron Church Road.

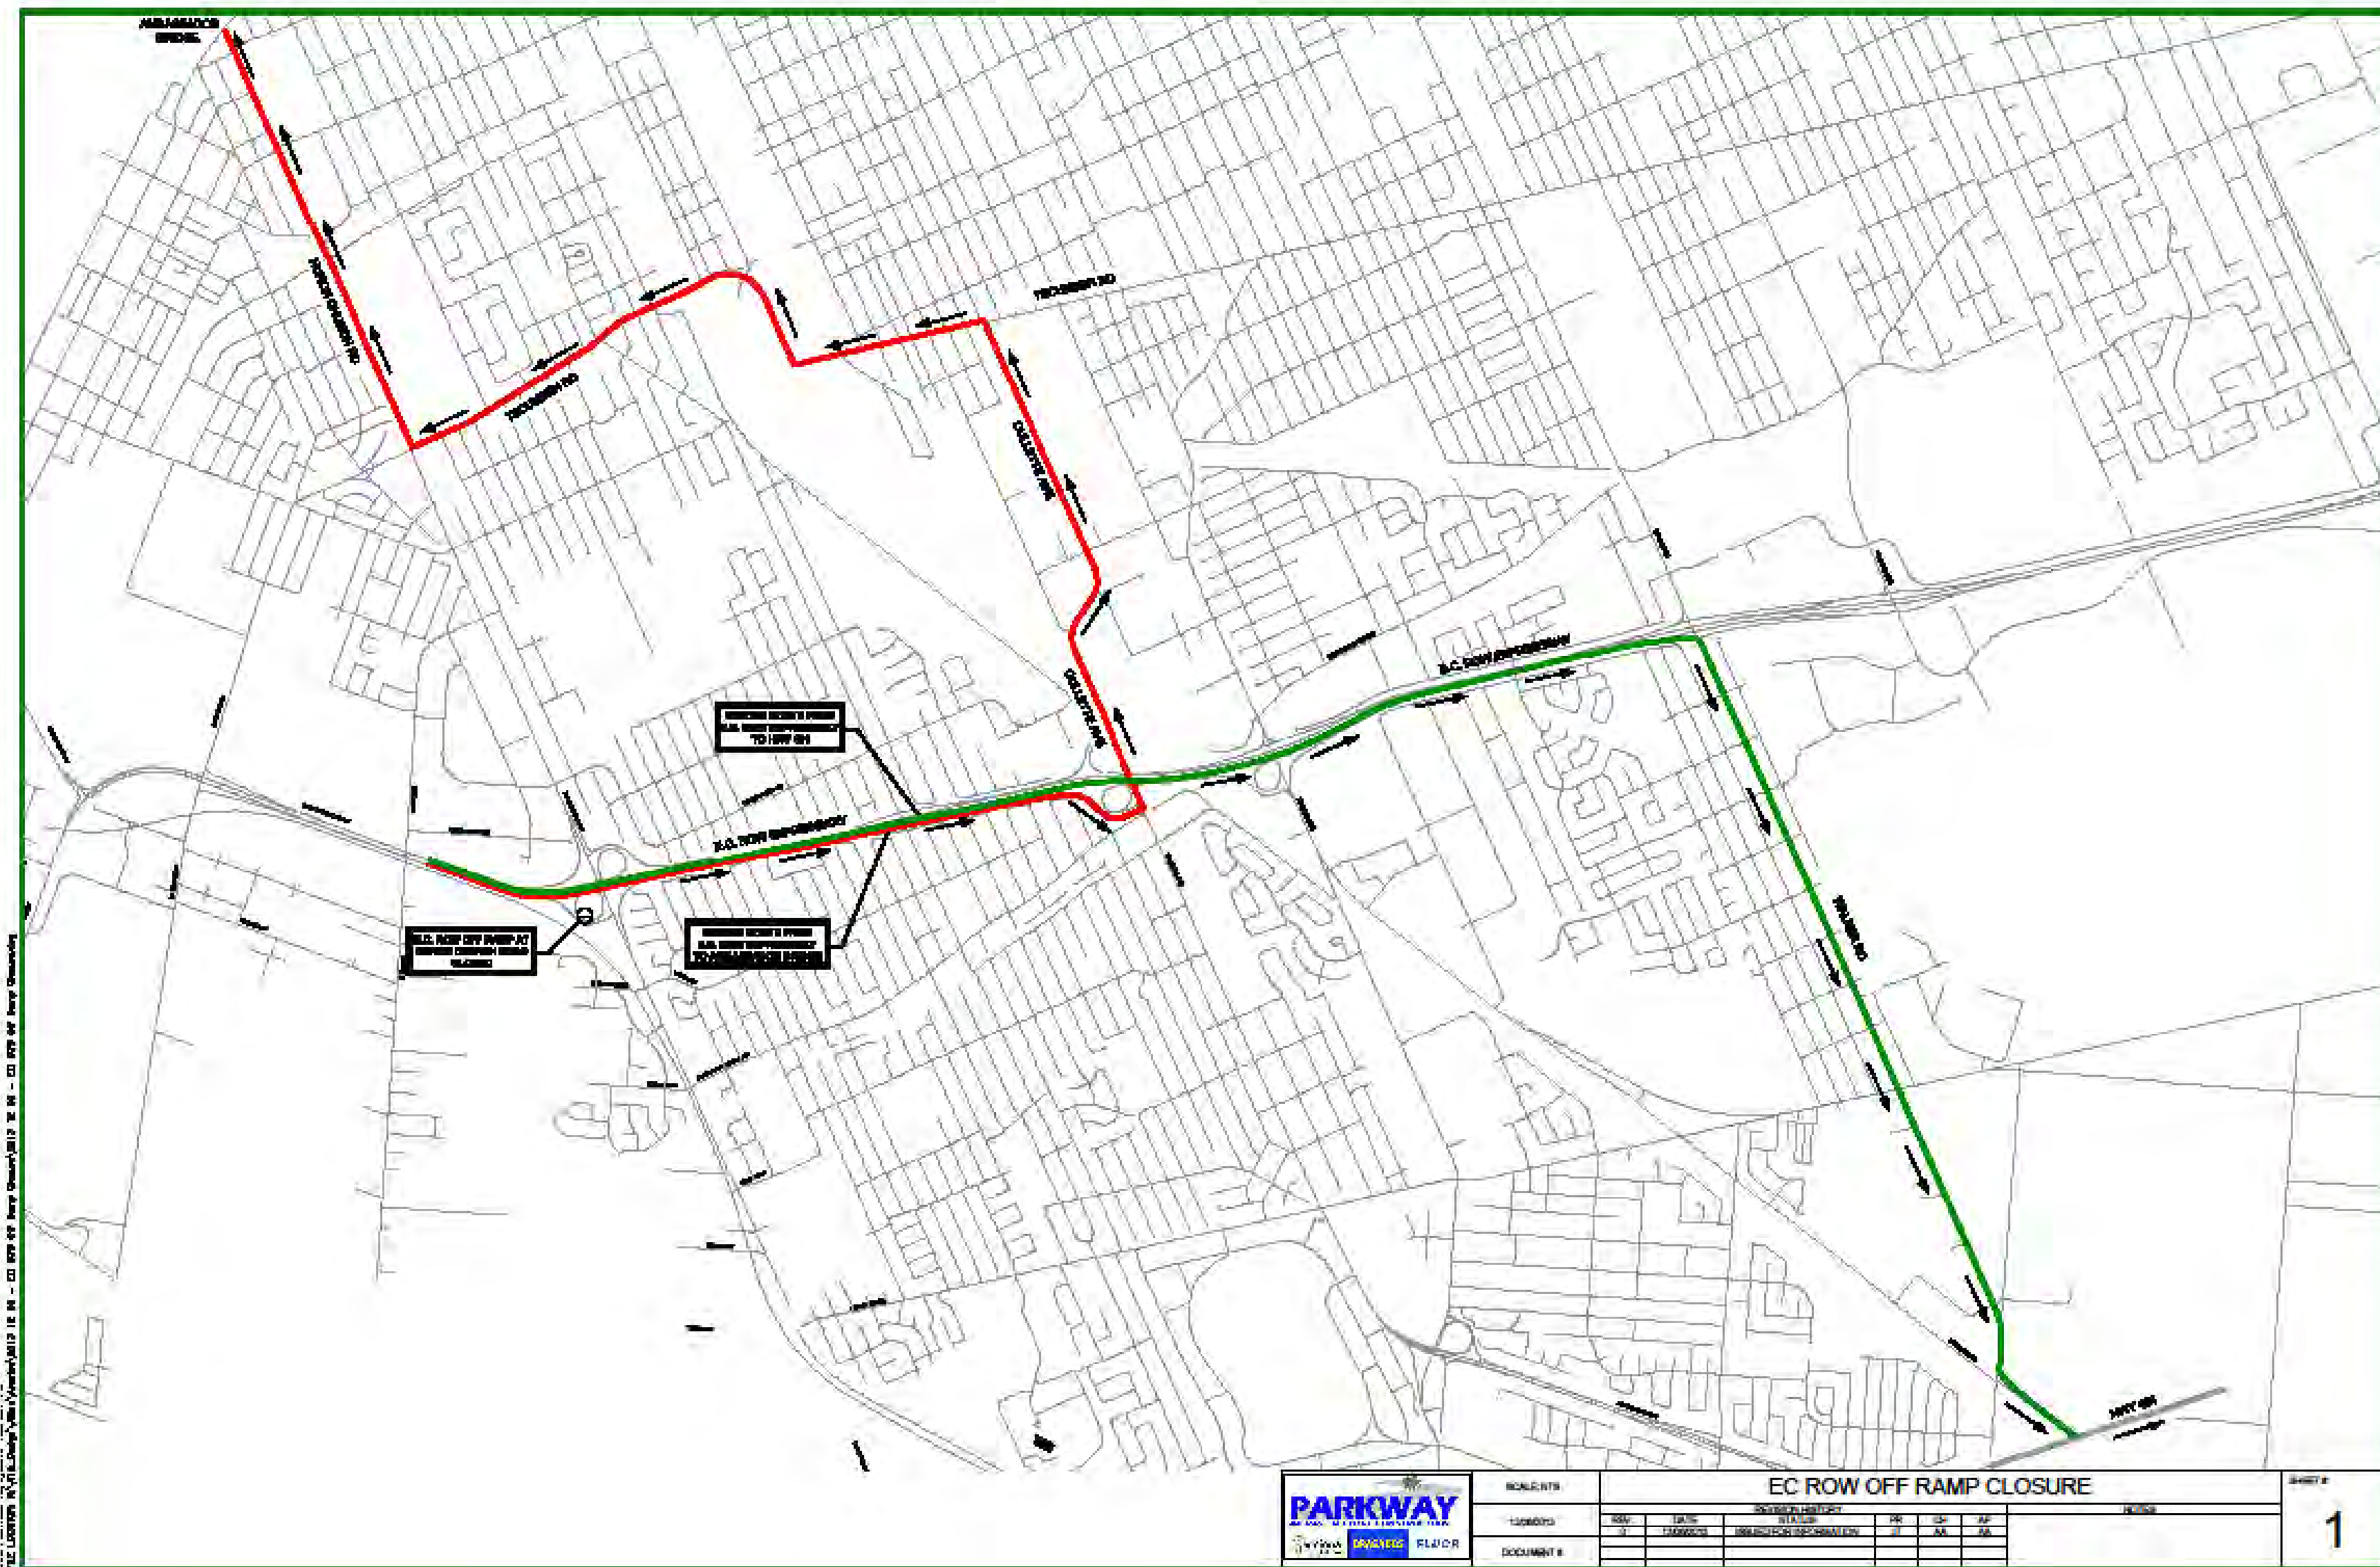

COMPLETED PERMANENT WORKS

#	WORKS	FROM	TO
1	Excavation for Highway 401	Todd Lane	West of Grand Marais Road West
		North of Labelle	Ojibway Parkway
2	Excavation for Highway 3	Howard Avenue	North of Grand Marais Road West

COMPLETED PERMANENT ROADS (OPEN TO TRAFFIC)

3	Highway 3	Howard Avenue	Todd Lane
		Pulford Street	Grand Marais Road West
4	Roundabout		
5	Outer Drive & Outer Drive Connector		
6	County Road 9 (Howard Diversion) & Howard Connector		

ONGOING WORKS

#	WORKS	FROM	TO
7	Roadworks for Highway 401	East End	West of Grand Marais Road West
		West of E.C. Row Expressway	East of Matchette Road
8	Roadworks for Highway 3	West of Cousineau Road	Pulford Street
9	Roadworks for E.C.Row Expressway	South of Huron Church Road	East of Matchette Road
10	Roadworks for intersection of Highway 3 and Howard Avenue		
11	Roadworks for Geraedts Drive		

UPCOMING WORKS

#	WORKS	FROM	TO	ANTICIPATED DATE
12	Demolition of Diversion 11	Geraedts Drive (St. Clair College)	New Highway 3	Winter 2014
13	Roadworks for Highway 401	Ojibway Parkway	East of Matchette Road	Spring 2014
14	Removal of D1-D2 Connector	Bethlehem Avenue	Huron Church Road	Fall 2014
15	Reconstruction of Bethlehem Avenue (T-2)	Bethlehem	Huron Church	Fall 2014
16	Reconstruction of Lambton Road (T-3)	Existing Lambton Road	Huron Church	Fall 2014
17	Reconstruction of Todd Lane (T-6)	Existing Todd Lane	Huron Church	Fall 2014
18	Reconstruction of Huron Church Line (T-7)	Existing Huron Church Line	Huron Church	Fall 2014

UPCOMING INSTALLATION OF NOISE WALLS			
#	FROM	TO	EXPECTED TIMING TO START INSTALLATION
19	East of Hearthwood Place	Montgomery Drive	December 2013
20	Montgomery Drive	East of Grosvenor Drive	December 2013
21	West of Howard Avenue	West of Shadetree Court	Winter 2014 & Fall 2014
22	West of Tunnel 10A (Villa Paradiso area)	East of Tunnel 10A (Villa Paradiso area)	Winter 2014
23	Behind St. Clair Avenue and Betts Avenue		Winter 2014
24	Villa Borghese area		Winter 2014
25	East of Lambton Road (Fazio area)	West of Pulford Street	Winter 2014

UPCOMING INSTALLATION OF NOISE WALLS			
#	FROM	TO	EXPECTED TIMING TO START INSTALLATION
26	North of Bethlehem Avenue	East of Bethlehem Avenue	Winter 2014
27	Spring Garden area		Spring 2014
28	From Ojibway	East of Matchette Road	Summer 2014
29	Chelsea area		Summer 2014
30	East side of Howard Avenue	South of Highway 3	Summer 2014
31	Howard Avenue	Havens Drive	Fall 2014
32	West of Homestead Lane	Tunnel 10B (Homestead Lane)	On hold
33	E.C. Row Expressway	Labelle Street	Pending on consultation
34	Labelle	East of Grand Marais	Pending on consultation

LANDSCAPE WORKS (Phase 1)

#	WORK	AREA	STATUS
A	Planting	From Sandwich West Parkway to Surrey Avenue	90% of trees and shrubs for roadside, screening and ecological typology have been planted
B	Planting	Pond 1, Pond 2, and Wolfe Drain	100% of trees and shrubs have been planted
C	Seed Mix Process	From Sandwich West Parkway to Surrey Avenue	Spring 2014
		Pond 1, Pond 2, and Wolfe Drain	
D	Winter Wheat Seed	All slopes	It is Temporary Winter Wheat Seed to Control Soil erosion

LANDSCAPE WORKS (Phases 2 & 3)

#	WORK	AREA	STATUS
E	Planting	From Cabana Road West to Ojibway Parkway	Trees and shrubs for roadside, screening and ecological typology to be planted in Spring 2014
F	Planting	Pond 6	100% of trees and shrubs have been planted
G	Seed Mix Process	Pond 6	Spring 2014
H	Winter Wheat Seed	All slopes	It is Temporary Winter Wheat Seed to Control Soil erosion
